

38

DART AEROSPACE LTD	Work Order:	21416
Description: Cross Bolt Spacer	Part Number:	D2579
Drawing: D2579 Rev. D	Qty:	500 536

Step	Location	Procedure	By	Date	Qty
1	EXPEDITING	Open W/O	HA	01.08.31	500
2	CNC-CELL	Machine as per Folio FA245 Material: 6061-T6 (WW-T-700/6) or 5052-H32 (WW-T-700/4) 0.500 Dia x 0.058 Wall Batch <u>M15483</u> SP 01/09/01 500 536	SP	01/09/01	536
3	QC	Inspect Level 2	SP	04/09/02	536
4	QC	Inspect Level 8	SP	04.09.02	536
5	STORES	Identify and stock	DP	04/09/02	536.
6	EXPEDITING	Inspect Level 21 Close W/O Cost / part: .76 suc 01/09/03 (536) 174	HA	04.09.07	536

Rev	Date	Change	Revised By	Approved
A	97.03.03	New Issue		
B	98.04.15	Eliminated deburring step	KB	
C	99.04.15	Added deburring step	DM	
D	01.06.04	Removed deburring step, added inspection level 21	EC	
E	02.06.17	Now turned on Cobra	NG RF	HA

RELEASED

02/06/17

Dart Aerospace Ltd

Work Order:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Manuf / Design Mgr	Approval QC Inspector

NCR		WORK ORDER NON-CONFORMANCE						
DATE	STEP	Description of NC section A	Corrective Action Section B		Sign & Date	Verification Section C	Approval Design Mgr	Approval QC Inspector
			Initial					

PAR#: _____ Fault Category: _____ DQA: _____ Date: _____


NOTE: Date & initial all entries
H:\Admin-QA\ISO\forms\w\oncB.doc

QA: N/C Closed: _____ Date: _____



DESIGN <i>RA</i>	DRAWN BY <i>RF</i>	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED <i>RA</i>	APPROVED <i>LE</i>	DRAWING NO. D2579	REV. D SHEET 1 OF 1
DATE 99.05.19		TITLE CROSS BOLT SPACER	SCALE 1:1
A	96.09.16	NEW ISSUE	
B	96.12.05	0.065 WALL WAS 0.035 WALL	
C	97.02.21	0.058 WALL WAS 0.065 WALL	
D	99.05.19	4.070 LENGTH WAS 4.100 (TSR A1095)	

RELEASED
99.05.20 DS

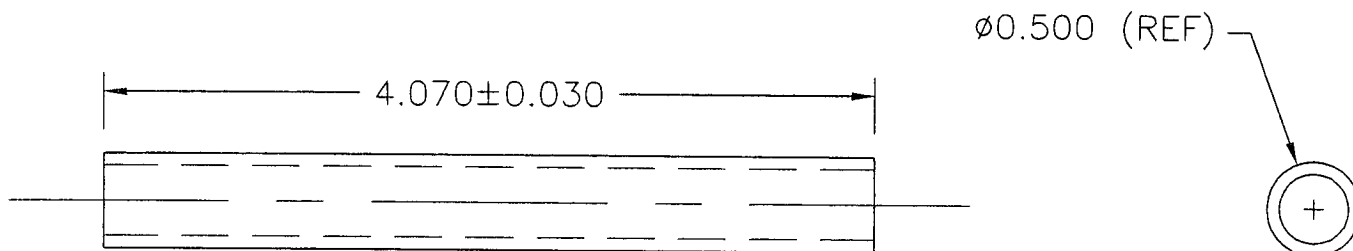

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 21416

MATERIAL: 6061-T6 (WW-T-700/6) OR 5052-H32 (WW-T-700/4)
0.500 DIA x 0.058 WALL
TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED

Job Costing Report

Dart Aerospace Ltd.
Hawkesbury

Aug 31, 2004
02:31 pm

Work Order No : 0021416
Project Name : D2579
Project For : WK438
Work Order Type : Main
Main WO Number :
House Part Number : D2579
Description : Crossbolt Spacer
Manufactured : Yes
Amount Req'd : 500
Amount Done : 0
Start Date : 08-31-04
Est Finish Date : 09-16-04
Act Finish Date :
Drawings Req'd : No
Ok for Approval :
Approval Rec'd :

Department Code:
Burden Flags : NNNNNNNN
WO Status : Open
Invoice State : Not Invoiced
Invoice Date :
Invoice Number :
Invoice Amount : 0.00
Order Entry No :
OE Value : 0.00
Est Margin : 0.000%
Actual Margin : 0.000%
\$0 Posted to Finished Goods

	Estimated	Actual	Var. %	Posted	To Post
Material Cost :	0.00	0.00	0.00	0.00	0.00
Engineering Hours :	0.00	0.00	0.00		
Engineering Cost :	0.00	0.00	0.00	0.00	0.00
Production Hours :	0.00	0.00	0.00		
Production Cost :	0.00	0.00	0.00	0.00	0.00
Packaging Hours :	0.00	0.00	0.00		
Packaging Cost :	0.00	0.00	0.00	0.00	0.00
OverHead Hours :	0.00	0.00	0.00		
OverHead Cost :	0.00	0.00	0.00	0.00	0.00
CNC Hours :	0.00	0.00	0.00		
CNC :	0.00	0.00	0.00	0.00	0.00
Misc. Hours :	0.00	0.00	0.00		
Misc. :	0.00	0.00	0.00	0.00	0.00
Burden :	0.00	0.00	0.00		
Total Cost :	0.00	0.00	0.00		
Margin :	0.000	0.000			
Selling Cost :	0.00	0.00			

	Estimated	Actual
Labour Hrs/Amount Done :	0.00	0.00
Profits/(Loss) :	0.00	0.00
